

Purchase Order Sundyne	PO00127118 / PNC 105 & PNC106
Sundyne Project	C23026: ADNOC Mechanical DGS Inconel / PCN105
Purchase EBF to EBG isnumbersued on the	2250087128 & 2200881927
Expected date of delivery	12/09/2025
Achievements level [estimate]	65%
Project status	Good way
Tasks:	Status
Order Acknowledgement issuing	Done
Project Set-up acc. PM, KPI	Done
Kick Off Meeting	Done
Po to sub-supplier / EBG	Done
Planning / project scheduling	In progress
LLI Purchasing	Done
Technical doc. Issuing / Client approval	In late
Fabrication	In progress
Mechanical Seals / DGS Testing	-----
Final pre-inspection for packing and shipment to GE	-----
Delivery date DAP (Sundyne)	-----
Financial	-----

Main points / Pain point

1 => Delivery of main DGS to Sundyne too late.


2 => EBF delivered the GAD to Sundyne in accordance with the MR datasheet the 1st/08.

3 => DGS PIM procedure : Not issued yet
=> Test procedure : EBF issued the new test procedure to Sundyne the 24/07
=> ITP : EBF closed the ITP
=> DATASHEET : Preliminary DGS issued a long the initial offer

EagleBurgmann.

a member of EKK and FREUDENBERG

Update: 21/08/2025

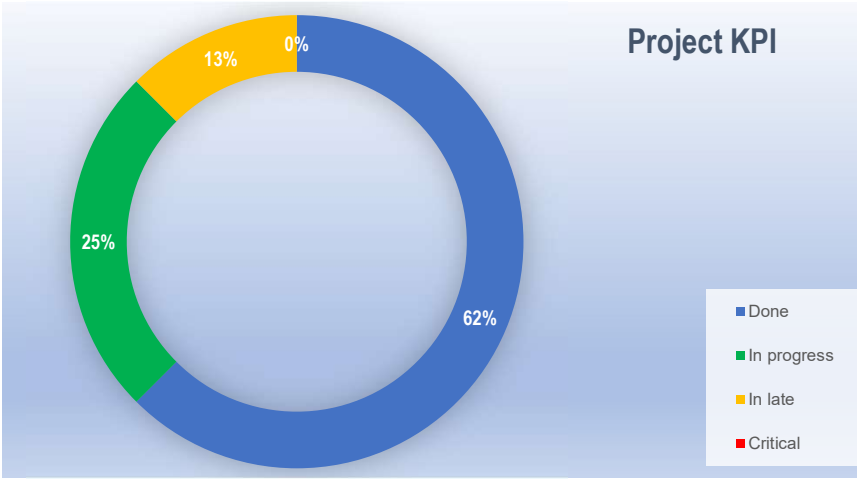

Risks / resolution

Key date of delivery to Sundyne for 50% on the 15th/10/2025 & 50% on the 1st/11/2025

Note: EBF is struggling to improve the delivery date reducing impacts of engineering phase. -Procurement time frame issues.

EBF is awaiting for official approval. Issued early in Augut.

- DGS PMI procedure : To be issued ASAP (delay due to summer holidays)
- Test procedure : Last update issued with Clirification sheet up to date on the 24th/07.
- ITP : Is closed
- DATASHEET : EBF will issue the DS to Sundyne by 22/08 at the latest

SOW & Main documentation

Item N°	Outcome	Description	Qty	EB part number	GAD doc number	ITP doc number	Test procedure doc number
1	DGS Main peices	Dry Gas Seals	4	1001362967	BUKA251/BUKA251+V30/V(2.4668)	2250087128_ITP_Rev1docx	TBA
2	DGS Spares	Dry Gas Seals	4	1001362967	BUKA251/BUKA251+V30/V(2.4668)		TBA
3		TBD	X				
4		TBD	X				
			X				

Special constraints

Designation	Comment	Designation	Comment
=> DGS data sheet	Issued with EBF offer for Sundyne comments. In february? EBF will issue the DS to Sundyne by 22/08 at the latest	=> PMI	AS per EagleBurgmann standard. Usually not issued to Client (EBG feedback)
=> DGS Dwg & 3D model step format	To be approved from Sundyne on the:03/06/2025	=> NACE	MR0175 certificates
=> DGS ITP	Rev1 issued to Sundyne on the 17th/06 for approval	=> Functional Test Procedure	API 692 with EB comments / minor deviations: Issued in last revision on the 24th/07
=> DGS PIM procedure	To be approved from Sundyne on the: Standard procdre to be issued by EB.	=> Seal Gas temperature	Design temperature clirified through Sundyne Material requisition and taken into account on the MS design and test procedure
=> 3.2 certificate	For inconel parts in contact with process: to be issued at the material delivery	=> DGS Test procedure	EBF issued with all tech calrifications put togetehr in CRS on the 24/07/25 with the updated doc.
=> 3.1 certificates	For metal part (1.4006) in contact with the process gaz: not trnsmitted yet. Could be shown during expediting visit	=> N/A	N/A

Notes / Remarks

a Sundyne inform EBG will receive a notification for an expediting visit. EBF was contacted by NMDC/ADNOC expeditor week 30. Contacted by 2 expeditors by email. No contact wih them this month and no request for expediting meeting to date.

b Production of seals started. Delivery planned for 50% on the 15th/10/25 & 50% on the 1st/11/25. EBG is impacted due to stock availability. No update on delivery dates since last confirmation given during last monthly meeting

General progress:

